



Facilities Update

Amador County Unified School District
May 23, 2018


Argonaut High Track



Argonaut High Culinary Arts



Amador High Stadium Solar Project

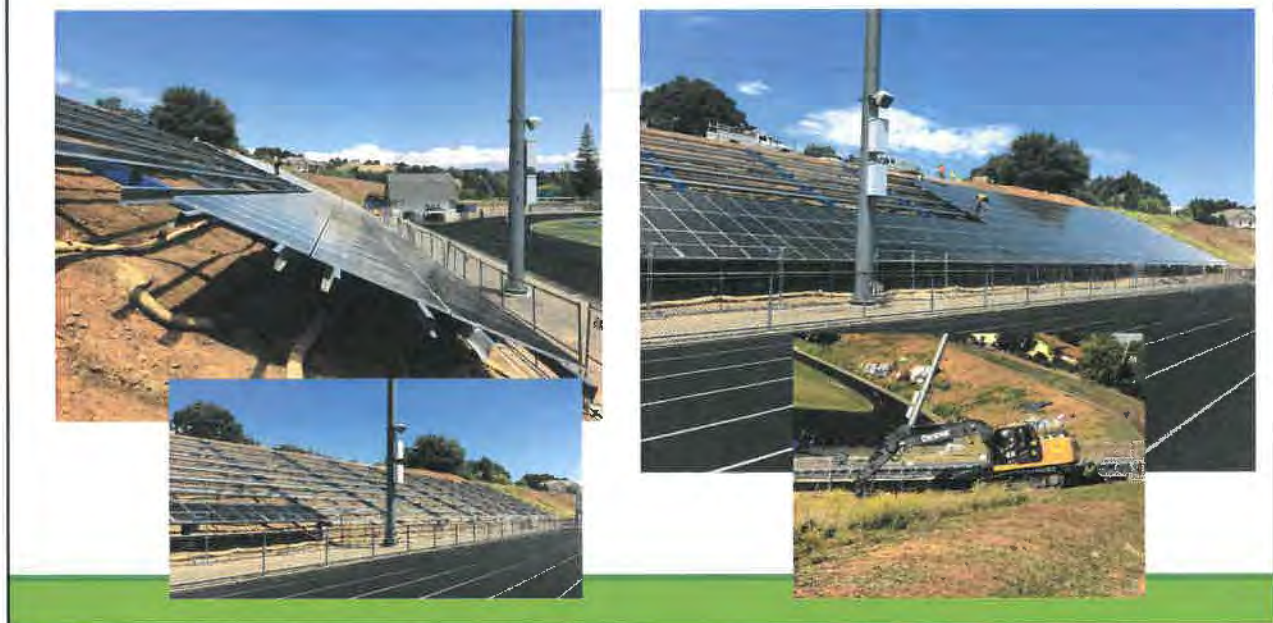

Project Timelines

- Argonaut High Track
 - All curbing to be completed by the end of this week
 - Gravel base will be installed next week
 - Paving scheduled for June 5 & 6
 - Rubber surface installation and painting will be completed in mid-July

- Argonaut High Culinary
 - Plumbing and electrical upgrades are complete
 - Hood vents have been installed and rooftop HVAC unit has been removed
 - Floor installation will be in mid-June
 - All appliances and equipment will be installed in mid-July

Project Timelines (cont.)

- Solar Project
 - Argonaut High solar field
 - Cleared for operation by Jackson Fire Department yesterday
 - Permission to operate should be granted by PG&E by the end of next week

 - Amador High stadium solar array
 - Panel installation will be completed by the end of the week
 - Electrical work will be completed by June 8
 - June 8 – PG&E inspection
 - Permission to operate is anticipated for mid to late June

